Delivery 1 - Load 1 of 2 - Artic 13.6 m

11 pallets in 5 of 5 floor positions | 220 forms | tallest column 2586 mm of 2650 mm inside height

Column heights do not fall to the tail: unload order was kept, which the crew needs, and it conflicts with loading tallest-forward on this load.

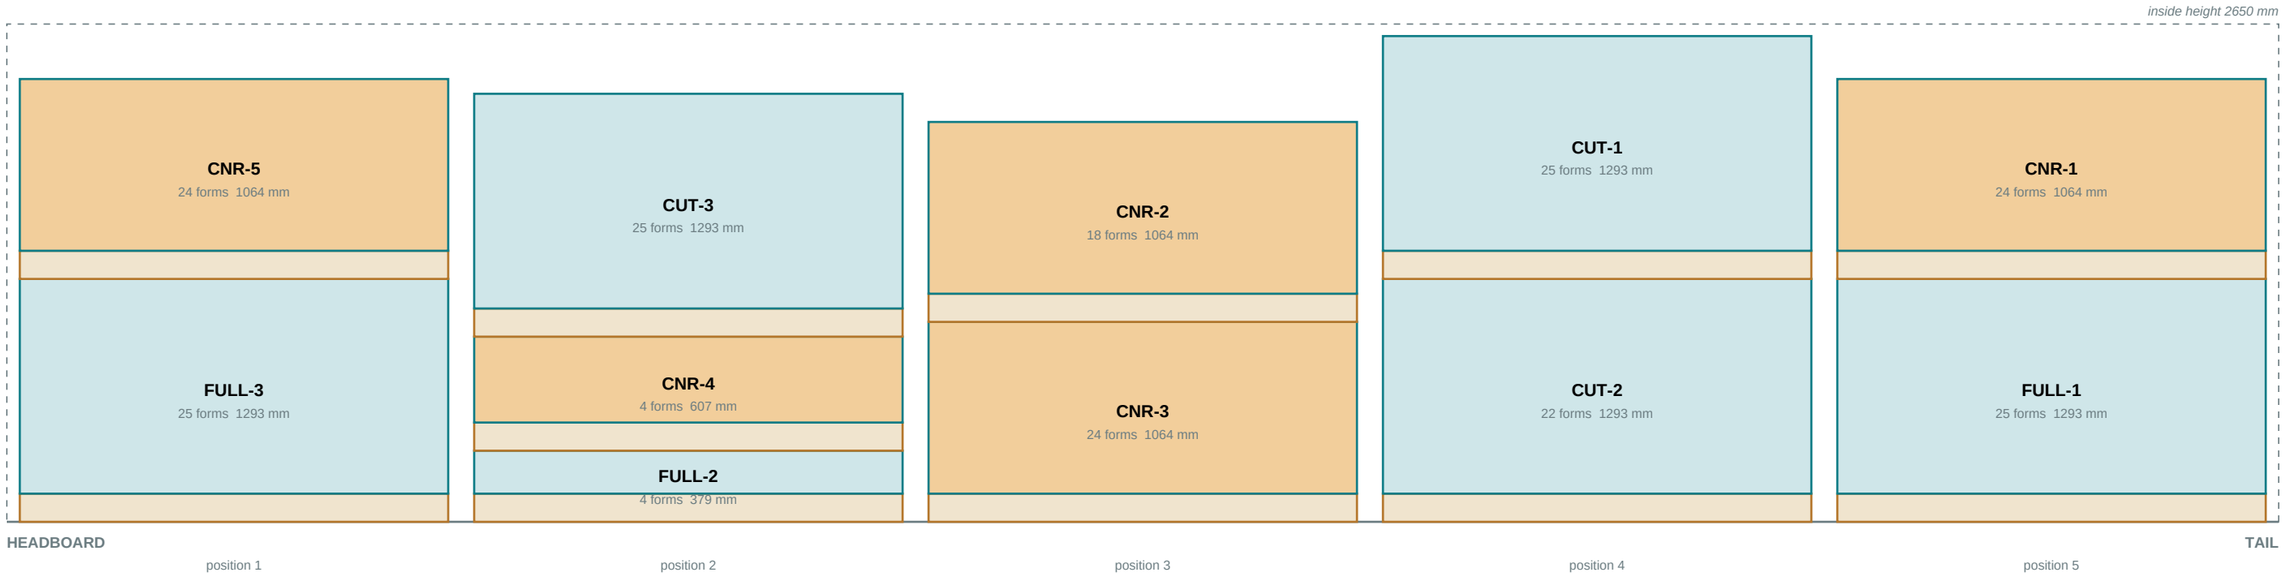

Unload order - 10 of 10 pallets come off out of build order, the price of stacking tallest forward

1. CNR-1 6in XR35 corners 24 forms courses B courses 1-5
2. FULL-1 6in XR35 straights 25 forms courses B courses 1-5
3. CUT-1 6in XR35 straights 25 forms courses B courses 1-6
4. CUT-2 6in XR35 straights 22 forms courses B courses 4-6
5. CNR-2 6in XR35 corners 18 forms courses B courses 5-6
6. CNR-3 6in XR35 corners 24 forms courses L1 courses 1-2
7. CUT-3 6in XR35 straights 25 forms courses L1 courses 1-2
8. CNR-4 6in XR35 corners 4 forms courses L1 course 2
9. FULL-2 6in XR35 straights 4 forms courses L1 course 2
10. CNR-5 6in XR35 corners 24 forms courses L2 courses 1-2
11. FULL-3 6in XR35 straights 25 forms courses L2 courses 1-3

Nudura™ **WAGON STACKING PLAN** **D1 LOAD 1**

Tallest column at the headboard; last needed on the floor

PROJECT	ES26-TBC-HR Insubloc - 67 Hendrefoilan Ro…	FORMS	220
VEHICLE	Artic 13.6 m	POSITIONS	5 of 5
PALLETS	11	TALLEST	2586 mm

Delivery 1 - Load 2 of 2 - Artic 13.6 m

3 pallets in 2 of 5 floor positions | 52 forms | tallest column 2357 mm of 2650 mm inside height

Column heights do not fall to the tail: unload order was kept, which the crew needs, and it conflicts with loading tallest-forward on this load.

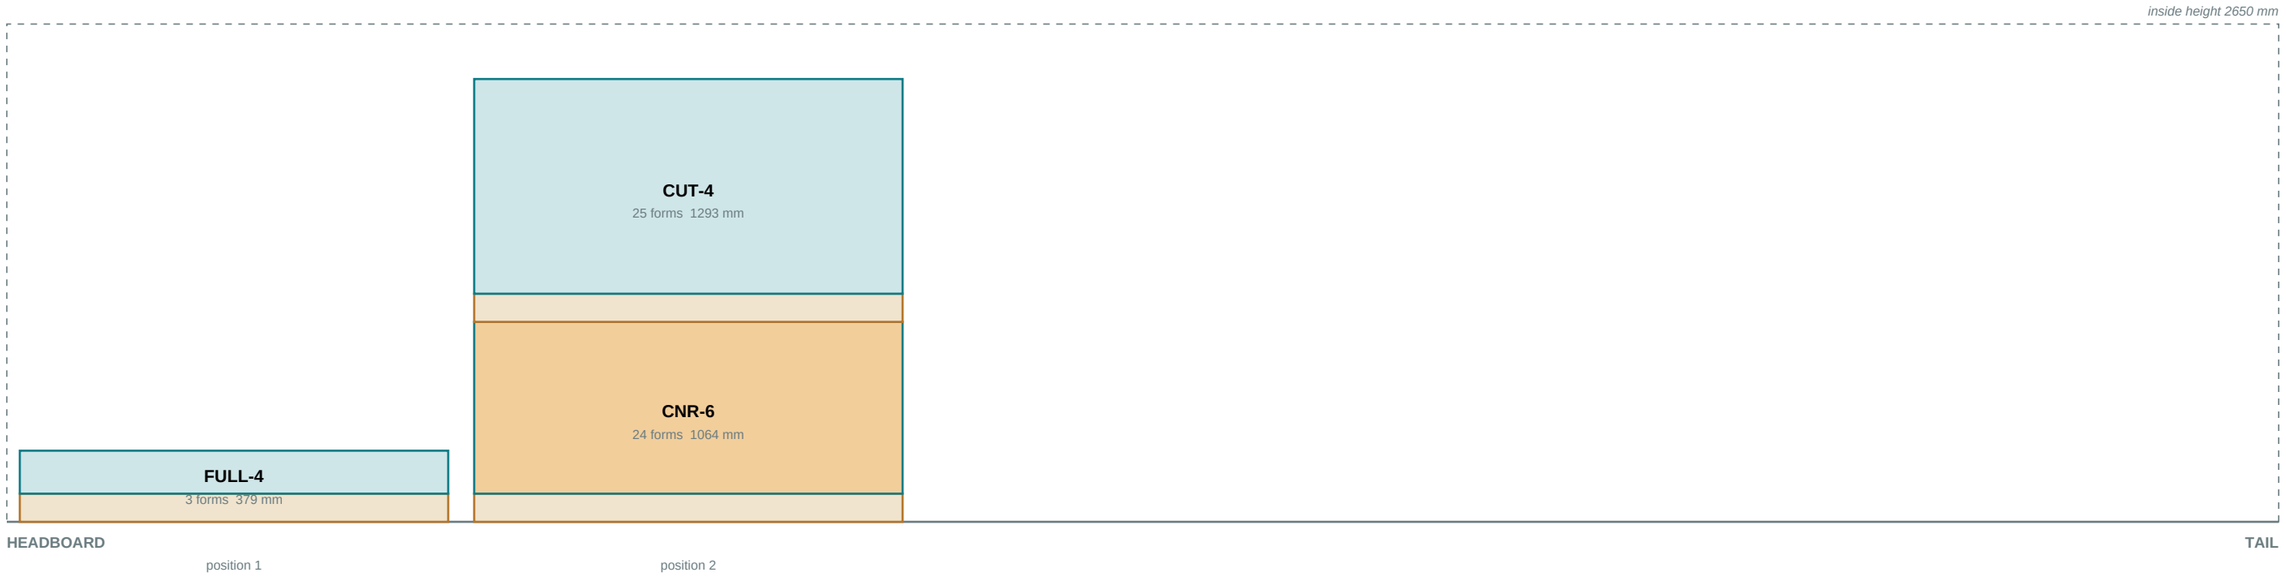

Unload order - 2 of 2 pallets come off out of build order, the price of stacking tallest forward

1. CUT-4 6in XR35 straights 25 forms courses L2 courses 1-4
2. CNR-6 6in XR35 corners 24 forms courses L2 courses 3-4
3. FULL-4 6in XR35 straights 3 forms courses L2 course 4

Nudura™ **WAGON STACKING PLAN** **D1 LOAD 2**

Tallest column at the headboard; last needed on the floor

PROJECT	ES26-TBC-HR Insubloc - 67 Hendrefoilan Ro…	FORMS	52
VEHICLE	Artic 13.6 m	POSITIONS	2 of 5
PALLETS	3	TALLEST	2357 mm

Delivery 2 - Load 1 of 1 - Artic 13.6 m

9 pallets in 4 of 5 floor positions | 198 forms | tallest column 2586 mm of 2650 mm inside height

Column heights do not fall to the tail: unload order was kept, which the crew needs, and it conflicts with loading tallest-forward on this load.

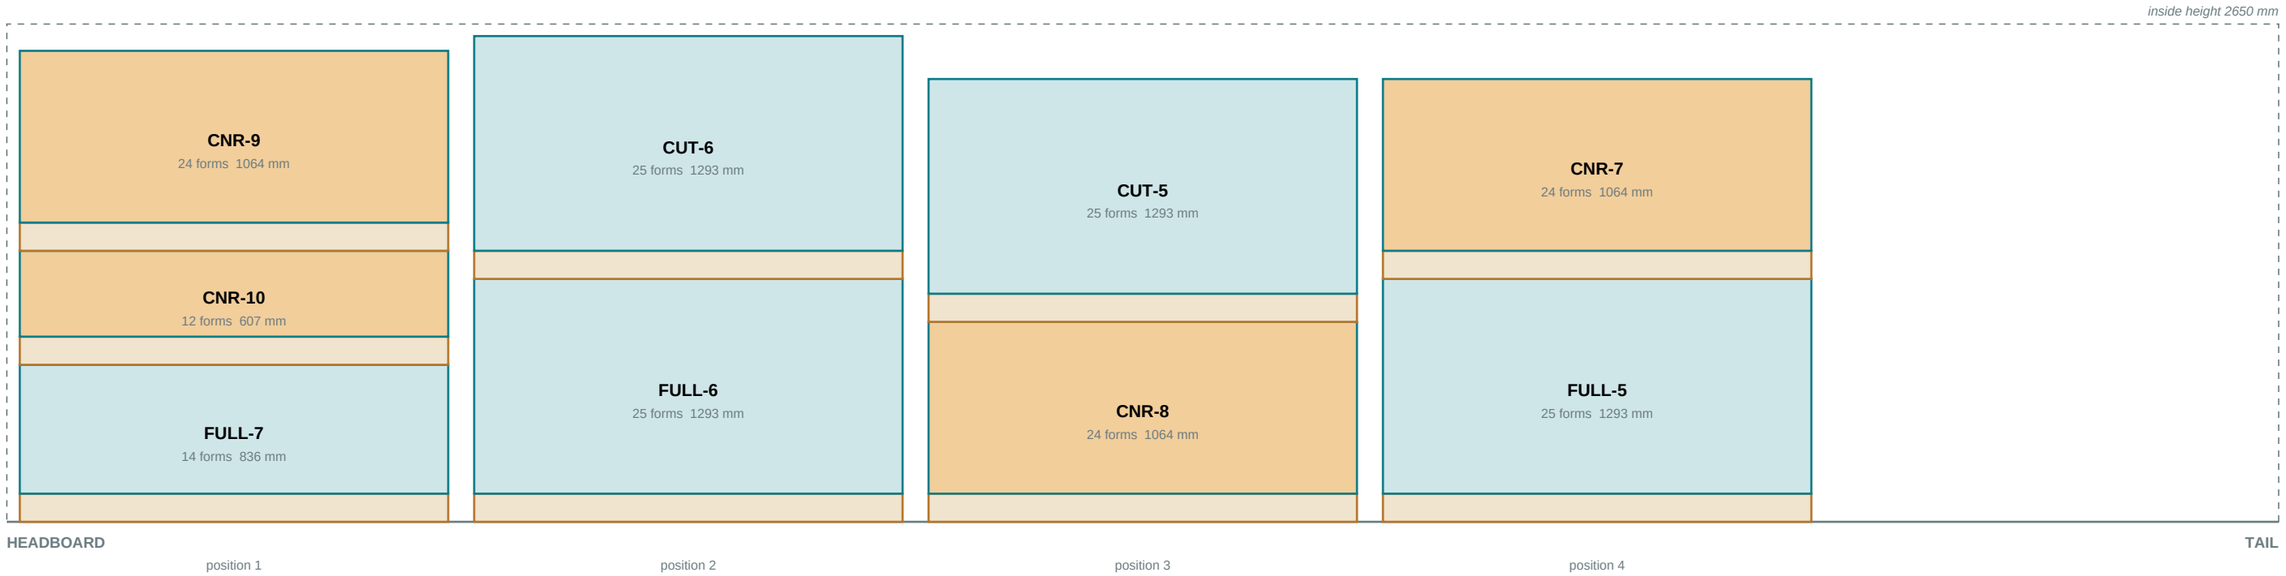

Unload order - 8 of 8 pallets come off out of build order, the price of stacking tallest forward

1. CNR-7 6in XR35 corners 24 forms courses L3 courses 1-2
2. FULL-5 6in XR35 straights 25 forms courses L3 courses 1-4
3. CUT-5 6in XR35 straights 25 forms courses L3 courses 1-12
4. CNR-8 6in XR35 corners 24 forms courses L3 courses 3-4
5. CUT-6 6in XR35 straights 25 forms courses L3 courses 3-13
6. FULL-6 6in XR35 straights 25 forms courses L3 courses 4-7
7. CNR-9 6in XR35 corners 24 forms courses L3 courses 5-6
8. CNR-10 6in XR35 corners 12 forms courses L3 course 7
9. FULL-7 6in XR35 straights 14 forms courses L3 courses 7-11

Nudura™ **WAGON STACKING PLAN** **D2 LOAD 1**

Tallest column at the headboard; last needed on the floor

PROJECT	ES26-TBC-HR Insubloc - 67 Hendrefoilan Ro…	FORMS	198
VEHICLE	Artic 13.6 m	POSITIONS	4 of 5
PALLETS	9	TALLEST	2586 mm
