
SUPPLY SCOPE (distributor quantities issue, no material prices): Nudura 6in XR35 walls - stepped base following the ground, GF + FF to the wall plate and the raked gables - pre-cut by BuildEase, stock forms and accessories by the distributor. Slabs, floor, steels, roofs, partitions and joinery are DESIGN ASSUMPTIONS drawn in good faith for coordination only (Wales - Approved Documents) - engineer / specialists to design.

QUOTATION - NOT FOR CONSTRUCTION

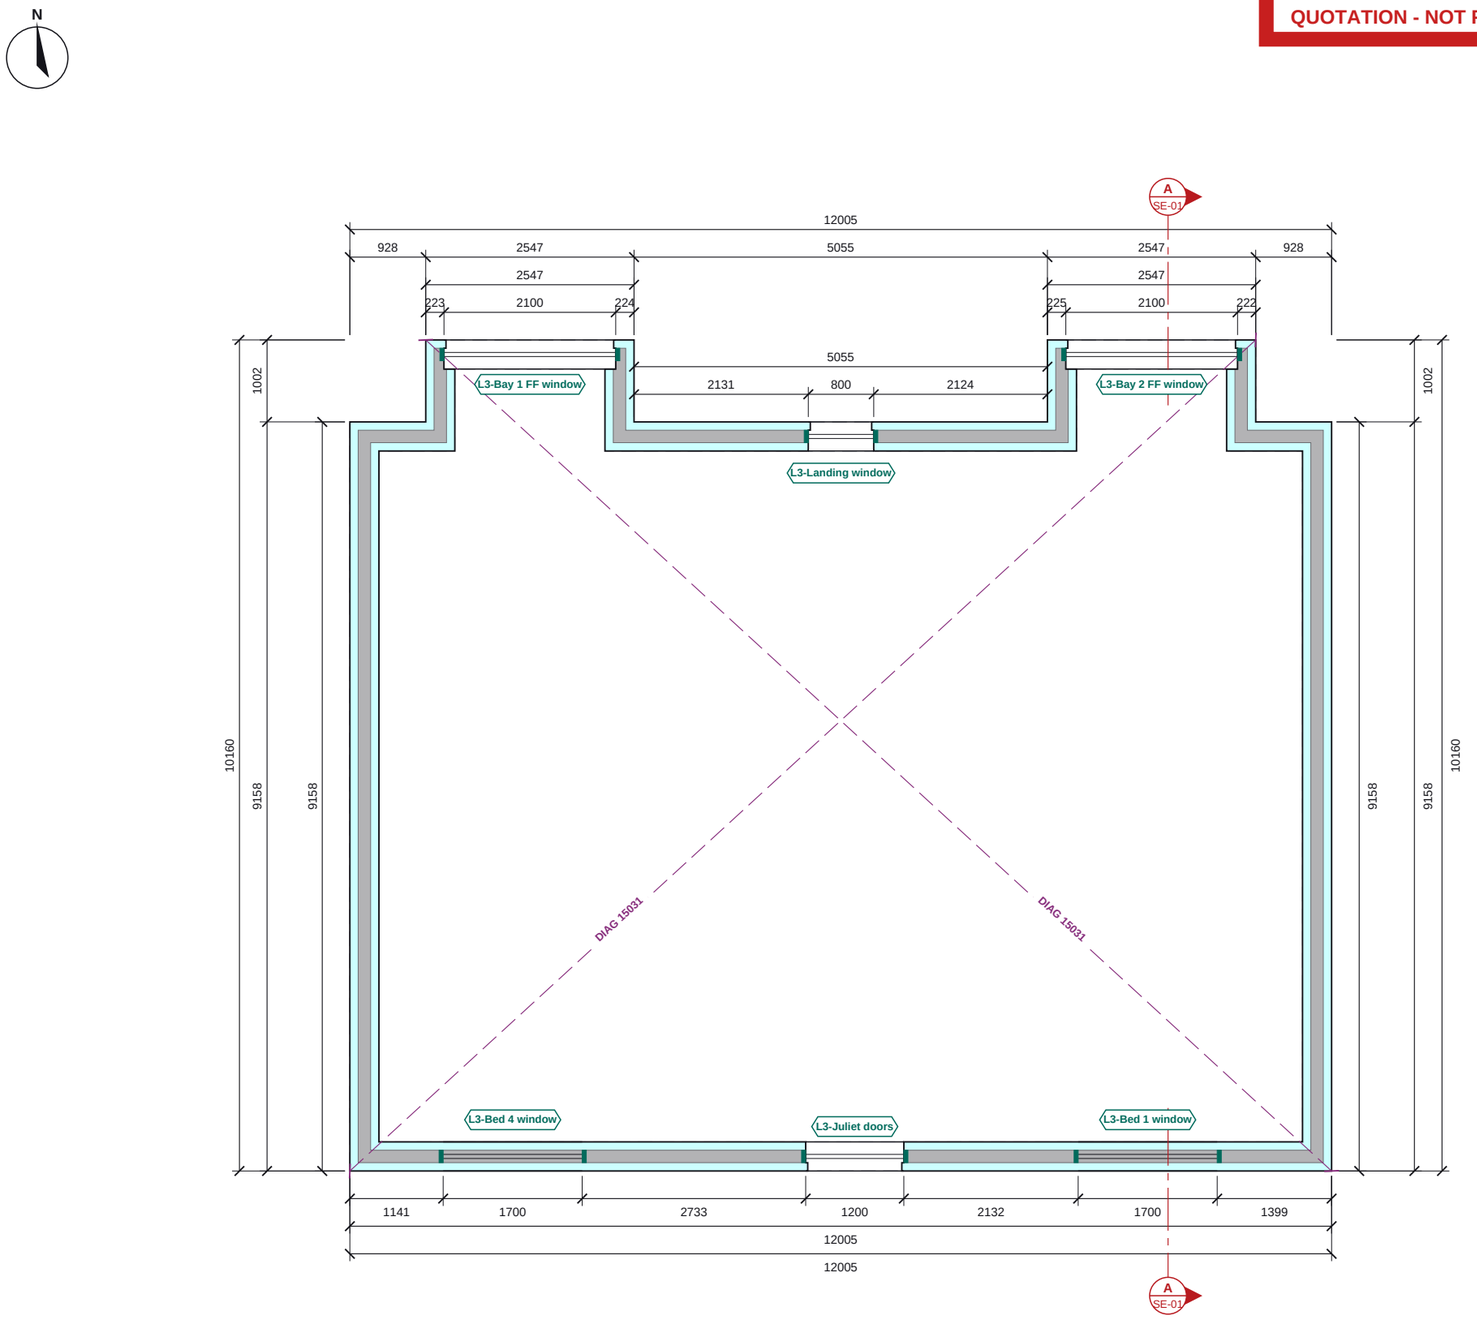

EPS insulation (Nudura form)
Concrete core
End cap at opening
ICF walls of the level below (dashed)
Engineer's pier bars (n-H12 vertical bars in ICF pier) / WS wall starters
Setting-out check diagonal (external ICF corners)
Section line (see SE sheet)

FIRST FLOOR + GABLES (ROOF TOOL CUTS EAVES TO THE PLATE, RAKES THE GABLES) ICF PLAN

Scale 1:75 @ A3 | Plan cut at +3753

0 1 2 3 4m

FIRST FLOOR + GABLES (ROOF TOOL CUTS EAVES TO THE PLATE, RAKES TH

OPENING SCHEDULE

Ref	Width	Height	Sill	Head	Lintel
L3-Bay 1 FF window	2100	1249	+3625	+4874	-
L3-Bay 2 FF window	2100	1249	+3625	+4874	-
L3-Landing window	800	1746	+3128	+4874	-
L3-Bed 4 window	1700	1050	+3877	+4927	-
L3-Juliet doors	1200	2075	+2852	+4927	-
L3-Bed 1 window	1700	1050	+3877	+4927	-

Structural openings in the ICF; sill and head above GF FFL.

NOTES

1. ICF: Nudura 6" XR35, 101.6 EPS + 152.4 core + 101.6 EPS = 355.6. Dimensions to the ICF faces.
2. Levels above GF FFL. Sill / head = structural opening in the ICF.
3. No structural design issued. 6in XR35 (152 core) walls from the planning drawings; the stepped base and the step-line wall retain up to ~1.8 m of fill - retaining design, reinforcement, lintels, the steels and the mix for the engineer.
4. Lintel (L-n) and steel (B-n, C-1) marks from rev -, which takes precedence.
5. Masonry walls shown for context.
6. Datum: 0 = front FFL. Kitchen-diner / extension FFL -1,500 (split level). FF FFL 2,850, wall plate 5,754.
7. From planning drawings 67SA2-12a / 67SA2-13 (no sections, no levels): levels and the ground line scaled from the 1:100 elevations - to be confirmed by a topo survey and the engineer.
8. The ICF base follows the falling ground 2 courses (914) below finished ground, stepping in whole courses.

REVISIONS

REV	DATE	DESCRIPTION
-	10.11.26	Quotation issue

Nudura™ BuildEase

CLIENT	PROJECT
Insubloc (distributor) - Tim Evans	67 Hendrefoilan Road, Sketty, Swansea SA2 9LU - Mr S Sparks

DRAWING TITLE
FIRST FLOOR + GABLES ICF GENERAL ARRANGEMENT - VERSION A (AS DRAWN)

SCALE	SIZE	DATE
1:75	A3	10.11.26
DRAWN	CHECKED	APPROVED
TS		

STATUS	DRAWING No.	REV
QUOTATION	ES26-089-GA-04A	-

Do not scale. All dimensions in millimetres, levels in metres from GF FFL. Check all dimensions on site.
