Delivery 1 - Load 1 of 2 - Artic 13.6 m

11 pallets in 5 of 5 floor positions | 218 forms | tallest column 2586 mm of 2650 mm inside height

Column heights do not fall to the tail: unload order was kept, which the crew needs, and it conflicts with loading tallest-forward on this load.

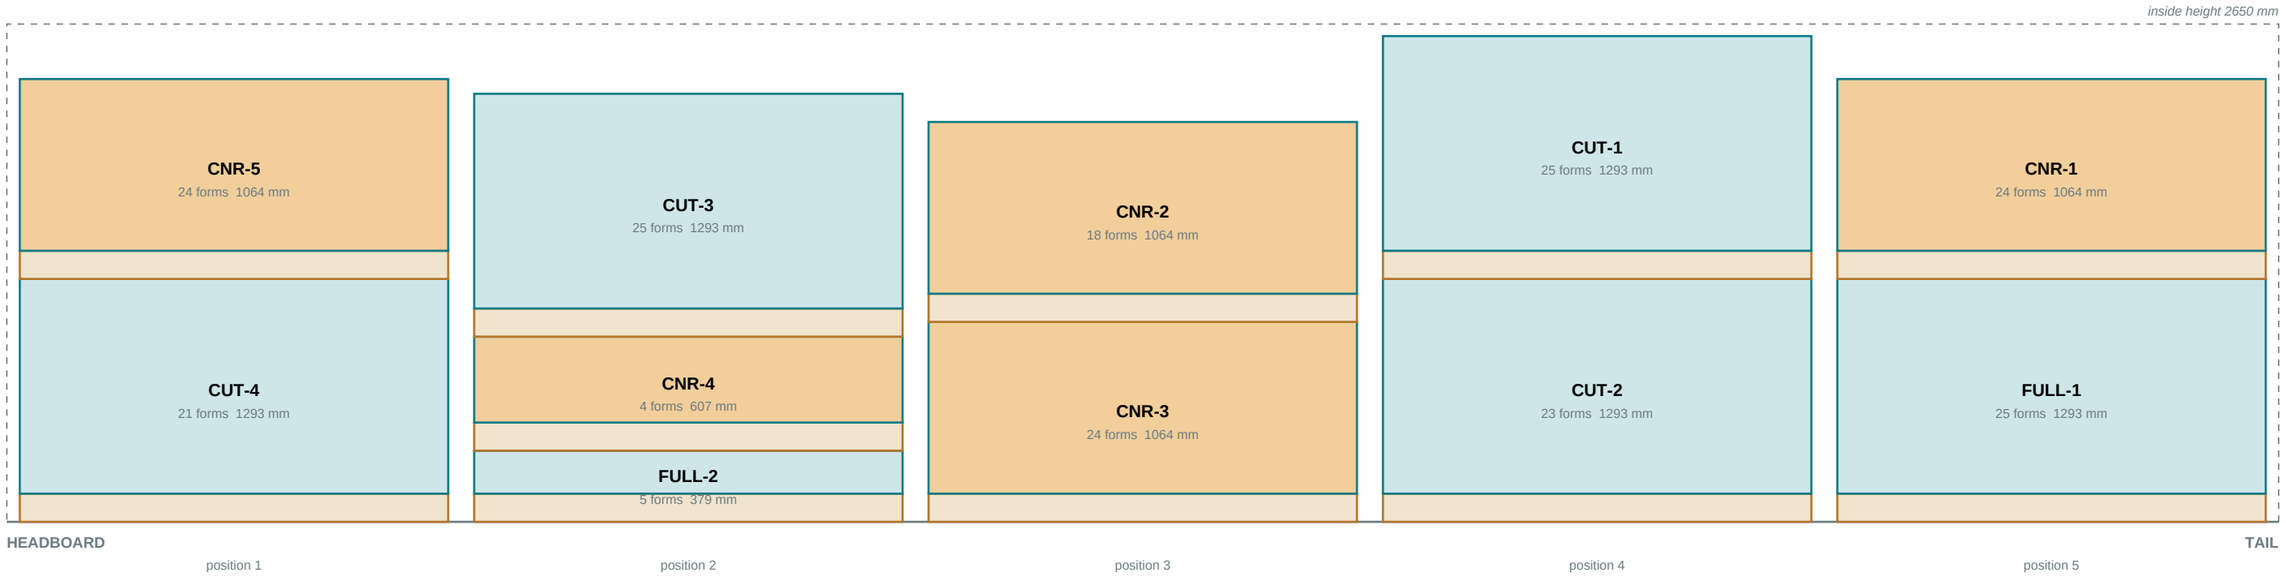

Unload order - 10 of 10 pallets come off out of build order, the price of stacking tallest forward

1. CNR-1 6in XR35 corners 24 forms courses B courses 1-5
2. FULL-1 6in XR35 straights 25 forms courses B courses 1-5
3. CUT-1 6in XR35 straights 25 forms courses B courses 1-6
4. CUT-2 6in XR35 straights 23 forms courses B courses 4-6
5. CNR-2 6in XR35 corners 18 forms courses B courses 5-6
6. CNR-3 6in XR35 corners 24 forms courses L1 courses 1-2
7. CUT-3 6in XR35 straights 25 forms courses L1 courses 1-2
8. CNR-4 6in XR35 corners 4 forms courses L1 course 2
9. FULL-2 6in XR35 straights 5 forms courses L1 course 2
10. CNR-5 6in XR35 corners 24 forms courses L2 courses 1-2
11. CUT-4 6in XR35 straights 21 forms courses L2 courses 1-4

Nudura™ **WAGON STACKING PLAN** **D1 LOAD 1**

Tallest column at the headboard; last needed on the floor

PROJECT	ES26-089 Insubloc - 67 Hendrefoilan Road, S…	FORMS	218
VEHICLE	Artic 13.6 m	POSITIONS	5 of 5
PALLETS	11	TALLEST	2586 mm

Delivery 1 - Load 2 of 2 - Artic 13.6 m

3 pallets in 2 of 5 floor positions | 61 forms | tallest column 2357 mm of 2650 mm inside height

Column heights do not fall to the tail: unload order was kept, which the crew needs, and it conflicts with loading tallest-forward on this load.

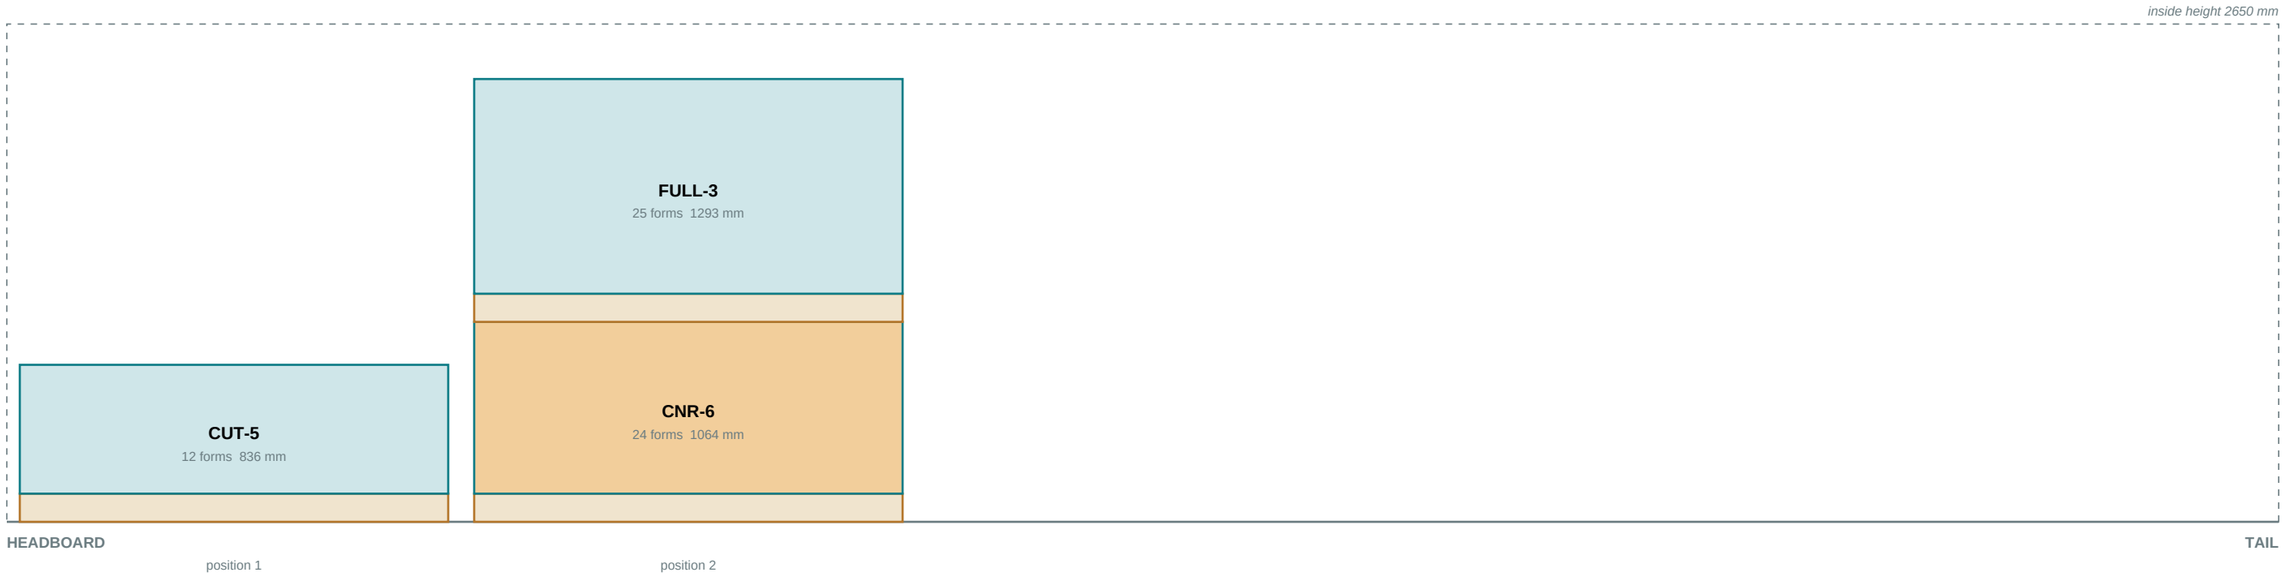

Unload order - 2 of 2 pallets come off out of build order, the price of stacking tallest forward

1. FULL-3 6in XR35 straights 25 forms courses L2 courses 1-4
2. CNR-6 6in XR35 corners 24 forms courses L2 courses 3-4
3. CUT-5 6in XR35 straights 12 forms courses L2 courses 3-4

Nudura™ **WAGON STACKING PLAN** **D1 LOAD 2**

Tallest column at the headboard; last needed on the floor

PROJECT	ES26-089 Insubloc - 67 Hendrefoilan Road, S…	FORMS	61
VEHICLE	Artic 13.6 m	POSITIONS	2 of 5
PALLETS	3	TALLEST	2357 mm

Delivery 2 - Load 1 of 1 - Artic 13.6 m

9 pallets in 5 of 5 floor positions | 205 forms | tallest column 2586 mm of 2650 mm inside height

Column heights do not fall to the tail: unload order was kept, which the crew needs, and it conflicts with loading tallest-forward on this load.

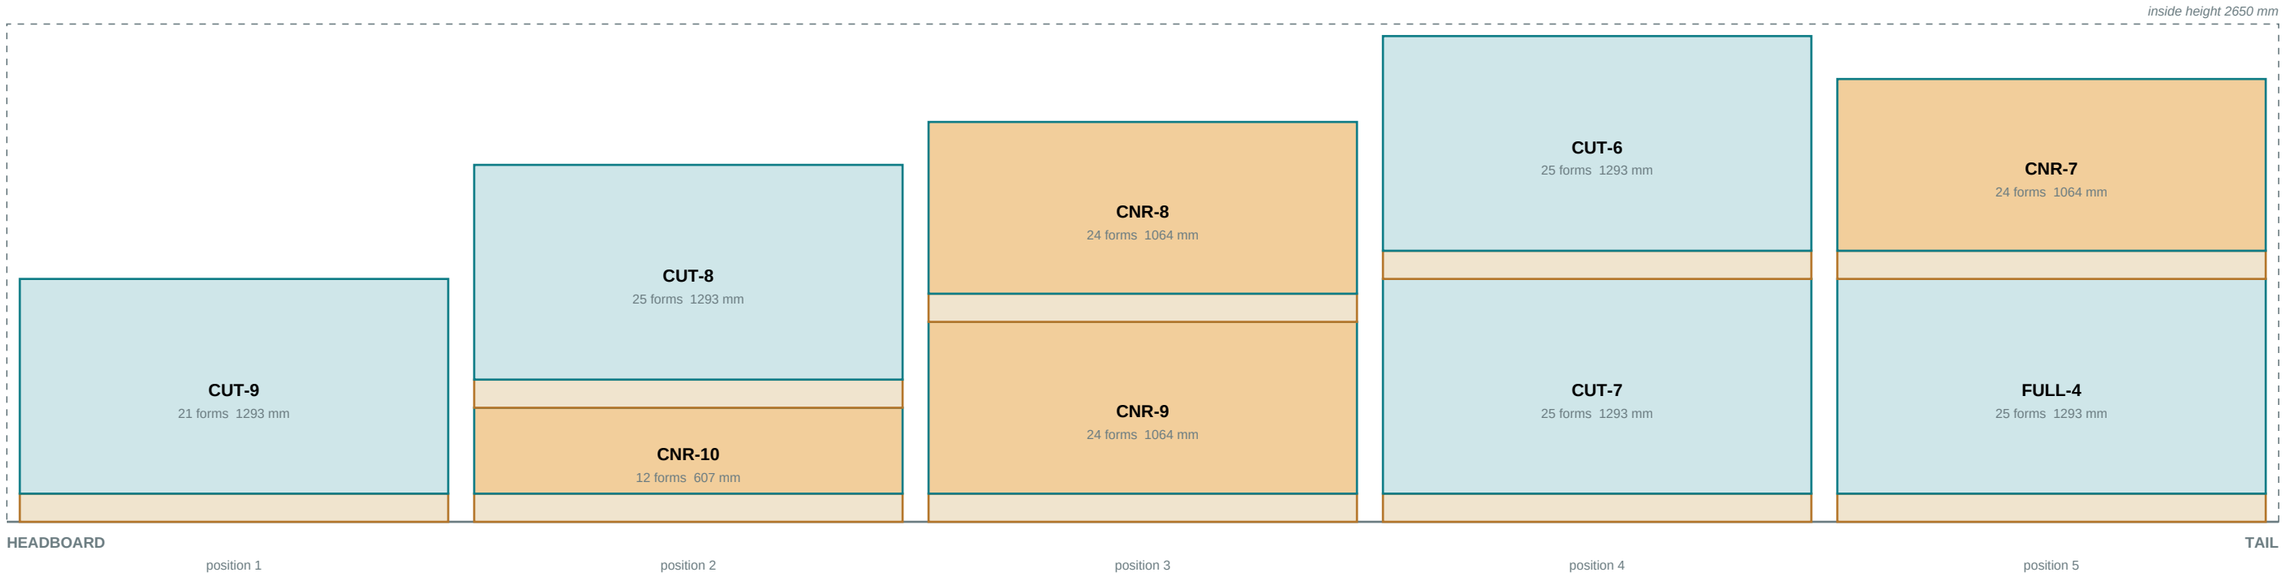

Unload order - 8 of 8 pallets come off out of build order, the price of stacking tallest forward

1. CNR-7 6in XR35 corners 24 forms courses L3 courses 1-2
2. FULL-4 6in XR35 straights 25 forms courses L3 courses 1-7
3. CUT-6 6in XR35 straights 25 forms courses L3 courses 1, 2, 3, 4, 6, 8, 9, 11, 12, 13
4. CUT-7 6in XR35 straights 25 forms courses L3 courses 2, 3, 4, 5, 6, 7, 8, 9, 10, 12
5. CNR-8 6in XR35 corners 24 forms courses L3 courses 3-4
6. CNR-9 6in XR35 corners 24 forms courses L3 courses 5-6
7. CUT-8 6in XR35 straights 25 forms courses L3 courses 5, 6, 7, 8, 9, 10, 12, 13
8. CNR-10 6in XR35 corners 12 forms courses L3 course 7
9. CUT-9 6in XR35 straights 21 forms courses L3 courses 7, 8, 9, 10, 11, 13

Nudura™ **WAGON STACKING PLAN** **D2 LOAD 1**

Tallest column at the headboard; last needed on the floor

PROJECT	ES26-089 Insubloc - 67 Hendrefoilan Road, S…	FORMS	205
VEHICLE	Artic 13.6 m	POSITIONS	5 of 5
PALLETS	9	TALLEST	2586 mm
